
Sample 30-min schedule

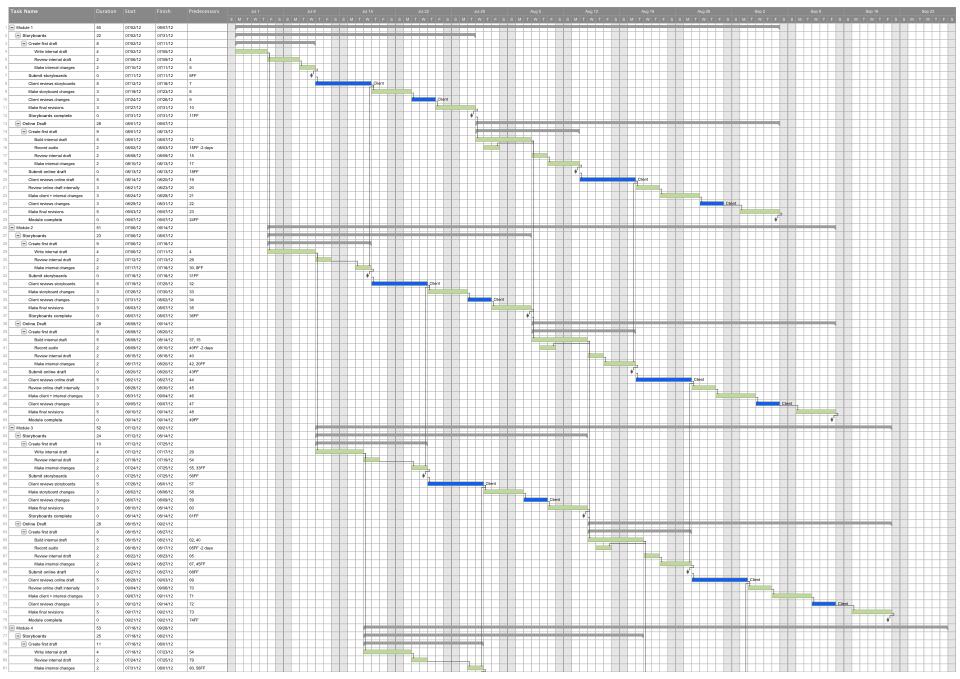

T	Task Name		Start	Finish	Predecessors	Jul 1			Jul 8			B Jul 15			Jul 22			Jul 29			Aug 5			Aug 12			A		Aug 19		Aug 26			Sep 2		Sep 2		Sep 9			Se				Sep 23				
_																																																	1
82	Submit storyboards	0	08/01/12	08/01/12	81FF														#°																														1
83	Client reviews storyboards	5	08/02/12	08/08/12	82																-		Cli	ent																									1
84	Make storyboard changes	3	08/09/12	08/13/12	83																					—																							1
85	Client reviews changes	3	08/14/12	08/16/12	84																							Client																					1
86	Make final revisions	3	08/17/12	08/21/12	85																																												1
87	Storyboards complete	0	08/21/12	08/21/12	86FF																																												1
88	Online Draft	28	08/22/12	09/28/12																														_	_	_		_		_	-	_	_		_			_	1
89	Create first draft	9	08/22/12	09/03/12																														_	_														1
90	Build internal draft	5	08/22/12	08/28/12	87, 65																																												1
91	Record audio	2	08/23/12	08/24/12	90FF -2 days																																												1
92	Review internal draft	2	08/29/12	08/30/12	90																																												1
93	Make internal changes	2	08/31/12	09/03/12	92, 70FF															ш																													1
94	Submit online draft	0	09/03/12	09/03/12	93FF																																												1
95	Client reviews online draft	5	09/04/12	09/10/12	94																																			Clien	1								1
96	Review online draft internally	3	09/11/12	09/13/12	95																																												1
97	Make client + internal changes	3	09/14/12	09/18/12	96																																												1
98	Client reviews changes	3	09/19/12	09/21/12	97																																								0	lient			1
99	Make final revisions	5	09/24/12	09/28/12	98																																											-	1
100	Module complete	0	09/28/12	09/28/12	99FF																																											+	1
